Unit 3 Part 2

Felicia Ainslie

Purdue University Global

Unit 3 Part 2

Meeting Recap

Meeting minutes			
Meeting Date	2/22/21	**Next Meeting Date**	3/2/21
Attendees	Ms. Ainslie Mr. Lyst Mr. Micro Mrs. Wan Mr. Fixit Ms. Perfect		
Agenda	• System analysis results. • MDM procurement and installation. • Remote staff network check results.		
Details			
Items	**Description**		**Presented by**
Item 1	Analysis results concluded new MDM and VPN were required.		Mr. Lyst
Item 2	MDM installation on schedule despite vendor contract delays.		Mr. Micro
Item 3	Network checks for remote staff concluded that minimal connectivity requirements are met.		Mrs. Wan
Next Steps			
Item Due Date	**Action**		**Responsible Party**
2/24/21	Finish updating operating systems and drivers on remote staff computers so web cams can be installed.		Mr. Fixit
2/25/21	Web cam Procurement		Mr. Fixit
2/23/21	Schedule network configuration with remote staff.		Mrs. Wan
2/26/21	Confirm the number of routers required.		Mrs. Wan
3/2/21	Procure 20 hotspots for remote staff with packet loss.		Mrs. Wan
3/1/21	Complete the VPN installation for all remote staff computers and setup user logins.		Mr. Micro
2/24/21	Test the MDM to ensure alerts work to advise leadership of compromising actions.		Ms. Perfect

Table 1. This table provides the details of the recent remote staff initiative project meeting.

Status Report

Status Report			
Tasks Completed	**Milestone**	**Accomplishments**	**Lessons Learned**
Analyze Hardware	Analysis	Current computers were in good condition for remote staff initiative.	N/A
Analyze Software	Analysis	Existing software did not accommodate the remote staff initiative.	No VPN or MDM was currently in use. Antivirus software was installed on computers and Active Directory was used to control/monitor resources. The available resources were inadequate for the remote staff initiative.
Create Contracts	AUP	Contracts were created with legal assistance to ensure remote staff were well informed of expectations and limitations.	Some staff members had mentioned privacy concerns such as if web cams would be used to watch staff. This was addressed in the contract to mitigate the risks of litigation in the future.
Contracts Signed	AUP	All 200 staff members accepted all details of the acceptable use policy.	N/A
Install MDM	Prepare Software	Sophos Unified Endpoint Management software was installed on all 200 computers.	N/A
Bandwidth	Network Check	Bandwidth was no less than 10GB on all 200 staff networks examined.	N/A
Latency	Network Check	Latency did not exceed 150ms on any of the 200 staff networks examined.	N/A
Packet loss	Network Check	Packet loss did not exceed 0% for 180 of the 200 staff networks examined.	Roughly 20 staff members had packet loss on their home network ranging from 1% to 10%. These individuals all shared a common backbone provider and may require a hotspot in the event the service causes disruptions in their work.

Table 2. This table provides an inside look on the current status of the remote support initiative.


WBS updates

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Milestone	Cost	% Work Complete
1		**Analysis**	**0 days**	**Wed 2/3/21**	**Wed 2/3/21**		**Mr. Lyst**	**Yes**	**$1,120.00**	**100%**
2		Analyze Hardware	2 days	Wed 2/3/21	Thu 2/4/21		Mr. Lyst	No	$560.00	100%
3		Analyze Software	2 days	Fri 2/5/21	Mon 2/8/21	2	Mr. Lyst	No	$560.00	100%
4		**AUP**	**0 days**	**Tue 2/9/21**	**Tue 2/9/21**	**3**	**Ms. Ainslie**	**Yes**	**$800.00**	**100%**
5		Create Contracts	2 days	Tue 2/9/21	Wed 2/10/21		Ms. Ainslie	No	$320.00	100%
6		Contracts Signed	3 days	Thu 2/11/21	Mon 2/15/21	5	Ms. Ainslie	No	$480.00	100%
7		**Prepare Hardware**	**0 days**	**Tue 2/16/21**	**Tue 2/16/21**	**6**	**Web Cams[0],Mr. Fixi**	**Yes**	**$1,792.00**	**50%**
8		Update Computers	7 days	Tue 2/16/21	Wed 2/24/21	6	Mr. Fixit	No	$896.00	75%
9		Install web cams	7 days	Thu 2/25/21	Fri 3/5/21	8	Mr. Fixit	No	$896.00	25%
10		**Prepare Software**	**0 days**	**Tue 2/16/21**	**Tue 2/16/21**	**6**	**VPN[0],MDM[0],Mr. I**	**Yes**	**$3,400.00**	**50%**
11		Install MDM	5 days	Tue 2/16/21	Mon 2/22/21	6	Mr. Micro	No	$1,680.00	100%
12		Install VPN	5 days	Tue 2/23/21	Mon 3/1/21	11	Mr. Micro	No	$1,680.00	0%
13		**Prepare Network**	**0 days**	**Tue 2/16/21**	**Tue 2/16/21**	**6**	**Cat5[0],Routers[0],Mı**	**Yes**	**$5,576.00**	**29%**
14		**Network Check**	**5 days**	**Tue 2/16/21**	**Mon 2/22/21**	**6**	**Mrs. Wan**	**No**	**$1,640.00**	**100%**
15		Bandwidth	5 days	Tue 2/16/21	Mon 2/22/21			No	$0.00	100%
16		Latency	5 days	Tue 2/16/21	Mon 2/22/21			No	$0.00	100%
17		Packet loss	5 days	Tue 2/16/21	Mon 2/22/21			No	$0.00	100%
18		**Configuration**	**5 days**	**Tue 2/23/21**	**Mon 3/1/21**	**14**	**Mrs. Wan**	**No**	**$1,640.00**	**0%**
19		Enable Multicast	5 days	Tue 2/23/21	Mon 3/1/21			No	$0.00	0%
20		Confirm No Double Nat	5 days	Tue 2/23/21	Mon 3/1/21			No	$0.00	0%
21		Firewall Rules	5 days	Tue 2/23/21	Mon 3/1/21			No	$0.00	0%
22		Disable SIP ALG	5 days	Tue 2/23/21	Mon 3/1/21			No	$0.00	0%
23		Install New Routers	7 days	Tue 3/2/21	Wed 3/10/21	18	Mrs. Wan	No	$2,296.00	0%

Figure 1. This image shows the first portion of the updated WBS.

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Milestone	Cost	% Work Complete
17		Packet loss	5 days	Tue 2/16/21	Mon 2/22/21			No	$0.00	100%
18		**Configuration**	**5 days**	**Tue 2/23/21**	**Mon 3/1/21**	**14**	**Mrs. Wan**	**No**	**$1,640.00**	**0%**
19		Enable Multicast	5 days	Tue 2/23/21	Mon 3/1/21			No	$0.00	0%
20		Confirm No Double Nat	5 days	Tue 2/23/21	Mon 3/1/21			No	$0.00	0%
21		Firewall Rules	5 days	Tue 2/23/21	Mon 3/1/21			No	$0.00	0%
22		Disable SIP ALG	5 days	Tue 2/23/21	Mon 3/1/21			No	$0.00	0%
23		Install New Routers	7 days	Tue 3/2/21	Wed 3/10/21	18	Mrs. Wan	No	$2,296.00	0%
24		**Testing**	**0 days**	**Mon 2/22/21**	**Mon 2/22/21**		**Ms. Perfect**	**Yes**	**$3,168.00**	**9%**
25		**Test MDM**	**2 days**	**Tue 2/23/21**	**Wed 2/24/21**	**11**	**Ms. Perfect**	**No**	**$576.00**	**50%**
26		Test Alerts	2 days	Tue 2/23/21	Wed 2/24/21			No	$0.00	0%
27		Test compromising MDM	2 days	Tue 2/23/21	Wed 2/24/21			No	$0.00	0%
28		**Test VPN**	**3 days**	**Tue 3/2/21**	**Thu 3/4/21**	**12**	**Ms. Perfect**	**No**	**$864.00**	**0%**
29		Resource Accessibility	3 days	Tue 3/2/21	Thu 3/4/21			No	$0.00	0%
30		Connectivity	3 days	Tue 3/2/21	Thu 3/4/21			No	$0.00	0%
31		Test Webcams	2 days	Tue 3/9/21	Wed 3/10/21		Ms. Perfect	No	$576.00	0%
32		Test Connectivity	2 days	Thu 2/25/21	Fri 2/26/21		Ms. Perfect	No	$576.00	0%
33		Test Access Controls	2 days	Fri 3/5/21	Mon 3/8/21		Ms. Perfect	No	$576.00	0%
34		**Assessments**	**0 days**	**Thu 3/11/21**	**Thu 3/11/21**		**Ms. Ainslie**	**Yes**	**$800.00**	**0%**
35		QA Review	2 days	Thu 3/11/21	Fri 3/12/21	24	Ms. Ainslie	No	$320.00	0%
36		Stakeholder Notice	1 day	Mon 3/15/21	Mon 3/15/21	35	Ms. Ainslie	No	$160.00	0%
37		Final Status	1 day	Tue 3/16/21	Tue 3/16/21	36	Ms. Ainslie	No	$160.00	0%
38		Lessons Learned	1 day	Wed 3/17/21	Wed 3/17/21	37	Ms. Ainslie	No	$160.00	0%

Figure 2. This image shows the second portion of the updated WBS.

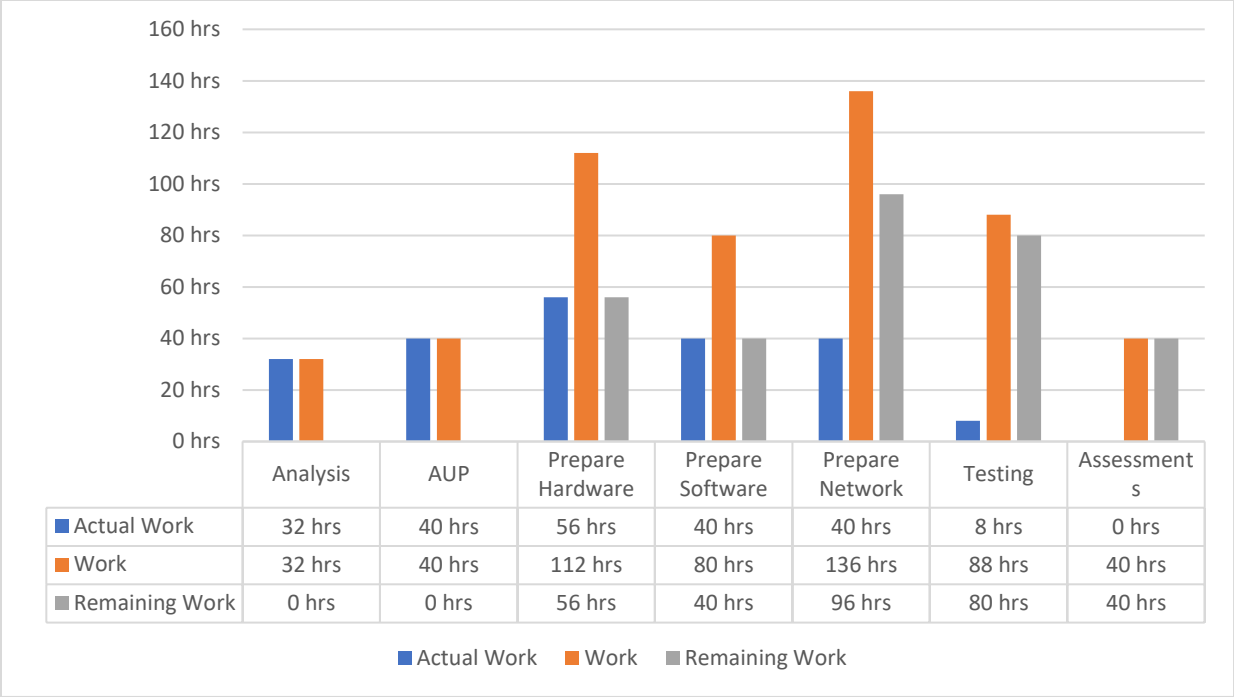

	Analysis	AUP	Prepare Hardware	Prepare Software	Prepare Network	Testing	Assessments
Actual Work	32 hrs	40 hrs	56 hrs	40 hrs	40 hrs	8 hrs	0 hrs
Work	32 hrs	40 hrs	112 hrs	80 hrs	136 hrs	88 hrs	40 hrs
Remaining Work	0 hrs	0 hrs	56 hrs	40 hrs	96 hrs	80 hrs	40 hrs

Figure 3. This image shows the anticipated workload, the amount completed, and the amount remaining for each milestone.

Current Budget

Remaining Cost	Actual Cost	Cost	Resource Names
$0.00	$1,120.00	$1,120.00	Mr. Lyst
$0.00	$800.00	$800.00	Ms. Ainslie
$896.00	$896.00	$1,792.00	Web Cams[0],Mr. Fixit
$1,680.00	$1,720.00	$3,400.00	VPN[0],MDM[0], Mr. Micro
$3,936.00	$1,640.00	$5,576.00	Cat5[0],Routers[0],Mrs. Wan
$2,880.00	$288.00	$3,168.00	Ms. Perfect
$800.00	$0.00	$800.00	Ms. Ainslie

Table 3. This table displays the current expenses are aligned with the anticipated costs.

Issues Register

Issue	Strategy	Date logged	Date resolved
MDM procurement was delayed as contract did not include all required features.	Worked with the vendor to correct contract in a timely manner so that 24/7 support would be available. Expressed need to begin installation on 2/16 and assistance was provided at no added cost to maintain schedule.	2/14/21	2/16/21
20 of the 200 staff members experienced packet loss between 1% and 10%.	Discovered a commonly shared backbone provider between the impacted staff members. This discovery lead to the assumption that this may be a reoccurring issue. Research is being completed to procure hotspots for the 20 staff members and is pending purchase to be added into the Prepare Network Milestone.	2/22/21	Still in progress with an estimated completion date of 3/10/21.

Table 4. This table outlines issues that were addressed thus far in the remote support initiative.
